FINAL SAY - PROJECT DEVELOPMENT TIMELINE


Evidence-based status with an explicitly estimated planning calendar

FinalSay monitors official institutional notices, extracts their content, compares versions, and presents a relationship result with provenance evidence.
The chart separates implementation status from dates: task windows are estimates, not reconstructed work logs.

REPORTING DATE	ESTIMATED PLANNING HORIZON	DATE BASIS
12 Nov 2026	**07 Sep - 15 Dec 2026**	**Actual project start/end and task completion dates are not established.**

DATED EVIDENCE CHECKPOINTS 07 Sep: earliest dated repository evidence (not project start) | 03 Nov: Phase 2 and Phase 3 reports | 10-11 Nov: source and integration updates | 12 Nov: current audit/tests

TASK / DELIVERABLE	START*	FINISH*	STATUS
PHASE 1 Research and Planning			COMPLETE
Problem identification and notice-risk use cases	07 Sep	13 Sep	Complete
Requirements and stakeholder needs	07 Sep	20 Sep	Complete
Literature and technology review	07 Sep	27 Sep	Complete
Scope definition and acceptance criteria	14 Sep	27 Sep	Complete
ML baseline and evaluation plan	21 Sep	04 Oct	Complete
PHASE 2 System Design			COMPLETE
Application architecture and API boundaries	21 Sep	04 Oct	Complete
Database entities, keys and version model	21 Sep	11 Oct	Complete
User roles and permission boundaries	28 Sep	11 Oct	Complete
Verification and reviewer workflow design	28 Sep	11 Oct	Complete
PHASE 3 Frontend Development			IN PROGRESS
Registration, login and auth context	05 Oct	25 Oct	In progress
Student submission and notices screens	12 Oct	02 Nov	Complete
Verification result and evidence interface	12 Oct	02 Nov	Complete
Reviewer queue, case and benchmark UI	19 Oct	02 Nov	Complete
Admin sources and provenance controls	19 Oct	09 Nov	Complete
Issuer notice-publishing interface	19 Oct	02 Nov	Complete
Full Admin analytics dashboard	23 Nov	07 Dec	Pending
PHASE 4 Backend Development			COMPLETE
Authentication APIs, JWT and role access	28 Sep	19 Oct	Complete
Notice APIs, database and version history	05 Oct	02 Nov	Complete
PDF/image upload and processing pipeline	12 Oct	02 Nov	Complete
Institution/source administration APIs	12 Oct	09 Nov	Complete
Issuer publishing and membership APIs	19 Oct	02 Nov	Complete
Frontend API integration and DB migrations	26 Oct	12 Nov	Complete

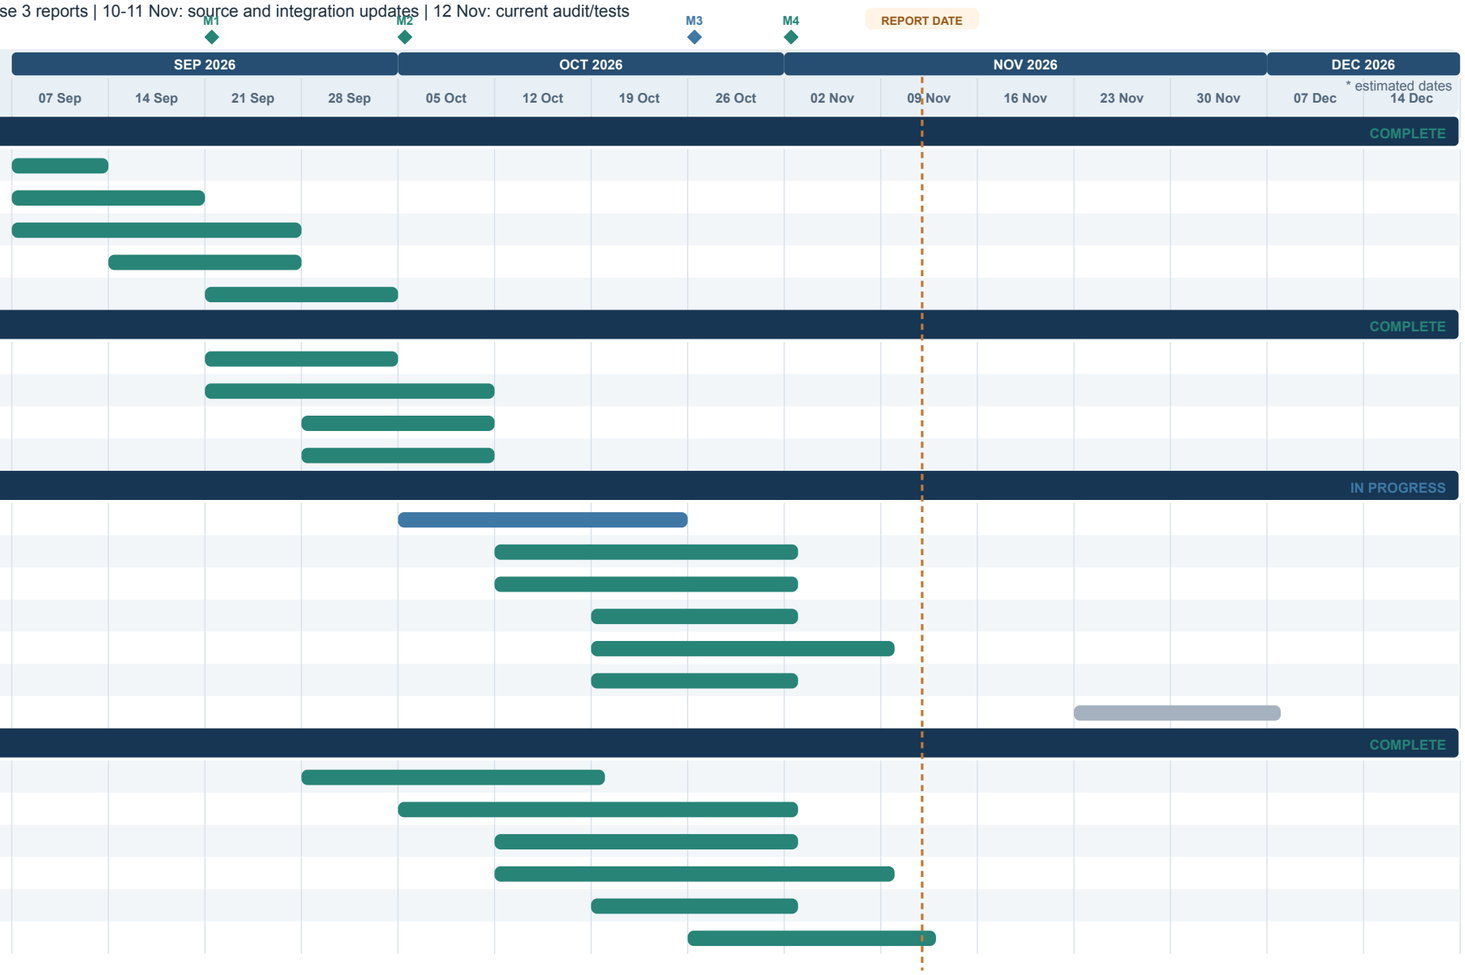

LEGEND Complete | In progress | Pending | Blocked | Estimated milestone target (M#) | Reporting date: 12 Nov 2026

Status is evidence-based as of the reporting date. A completed code/test milestone does not claim production deployment or real-user validation.

Historical boundary: no Git metadata is present in this checkout. Dates after the report date are planning estimates, not commitments.

Key dependencies: API/database -> retrieval and comparison; supported adapters -> backfill; contract + reachable RPC and configured wallet -> public anchoring.


Real-user end-to-end validation requires stable source polls and real accounts; production deployment requires cloud credentials, managed PostgreSQL, TLS and monitoring.

FINAL SAY - PROJECT DEVELOPMENT TIMELINE

PHASES 5-9 - ML VERIFICATION, SOURCE INGESTION, PROVENANCE, TESTING AND DELIVERY

Estimated task windows; statuses reflect code, tests, dated reports, and local database evidence available by 12 Nov 2026.

TASK / DELIVERABLE	START*	FINISH*	STATUS
PHASE 5 AI-Based Notice Verification			COMPLETE
PDF text extraction and bounded OCR fallback	05 Oct	02 Nov	Complete
Image OCR, preprocessing and field extraction	05 Oct	02 Nov	Complete
Text normalization, redaction and hashing	05 Oct	26 Oct	Complete
Semantic candidate retrieval	12 Oct	02 Nov	Complete
DeBERTa NLI relation classifier and evidence	19 Oct	09 Nov	Complete
Superseded/contradictory/unresolved integration	26 Oct	11 Nov	Complete
Hosted LLM verification integration	01 Dec	15 Dec	Pending
PHASE 6 Web Scraping and Official Sources			IN PROGRESS
Automatic discovery / arbitrary-site crawling	01 Dec	15 Dec	Pending
Six typed source adapters and onboarding	19 Oct	09 Nov	Complete
HTML/JSON notice listing and pagination	19 Oct	09 Nov	Complete
PDF discovery, extraction and sidecar refresh	26 Oct	23 Nov	In progress
VTU, Delhi and Mumbai live source integration	02 Nov	23 Nov	In progress
Source-key duplicate detection and revisions	26 Oct	09 Nov	Complete
Allowlist, HTTPS, robots and bounded requests	26 Oct	09 Nov	Complete
Historical backfill and poll reliability	02 Nov	01 Dec	In progress
PHASE 7 Blockchain and Provenance			BLOCKED
SHA-256, Merkle proofs and local hash chain	28 Sep	03 Nov	Complete
Solidity contract and Foundry test suite	26 Oct	03 Nov	Complete
Amoy adapter, receipt and contract read-back	26 Oct	03 Nov	Complete
Public RPC, wallet setup and testnet deployment	03 Nov	07 Dec	Blocked
Provenance API and Admin/Student displays	26 Oct	03 Nov	Complete
PHASE 8 System Integration and Testing			IN PROGRESS
Role-based frontend/backend integration	26 Oct	09 Nov	Complete
Backend auth, API and regression suite	02 Nov	12 Nov	Complete
OCR, semantic, scraping and contract tests	02 Nov	12 Nov	Complete
Controlled cross-URL supersession workflow	03 Nov	11 Nov	Complete
Real student and reviewer end-to-end validation	12 Nov	30 Nov	Pending
Live source and registration issue follow-up	10 Nov	30 Nov	In progress
PHASE 9 Deployment and Finalization			PENDING
Docker, Compose, Pages and ECS configuration	26 Oct	12 Nov	Complete
Production secrets, PostgreSQL, TLS and monitoring	16 Nov	07 Dec	Pending
Performance evaluation and pilot readiness	23 Nov	07 Dec	Pending
Security findings remediation	12 Nov	07 Dec	In progress
Technical documentation and demo script	02 Nov	12 Nov	Complete
Cloud deployment and final project demonstration	01 Dec	15 Dec	Pending

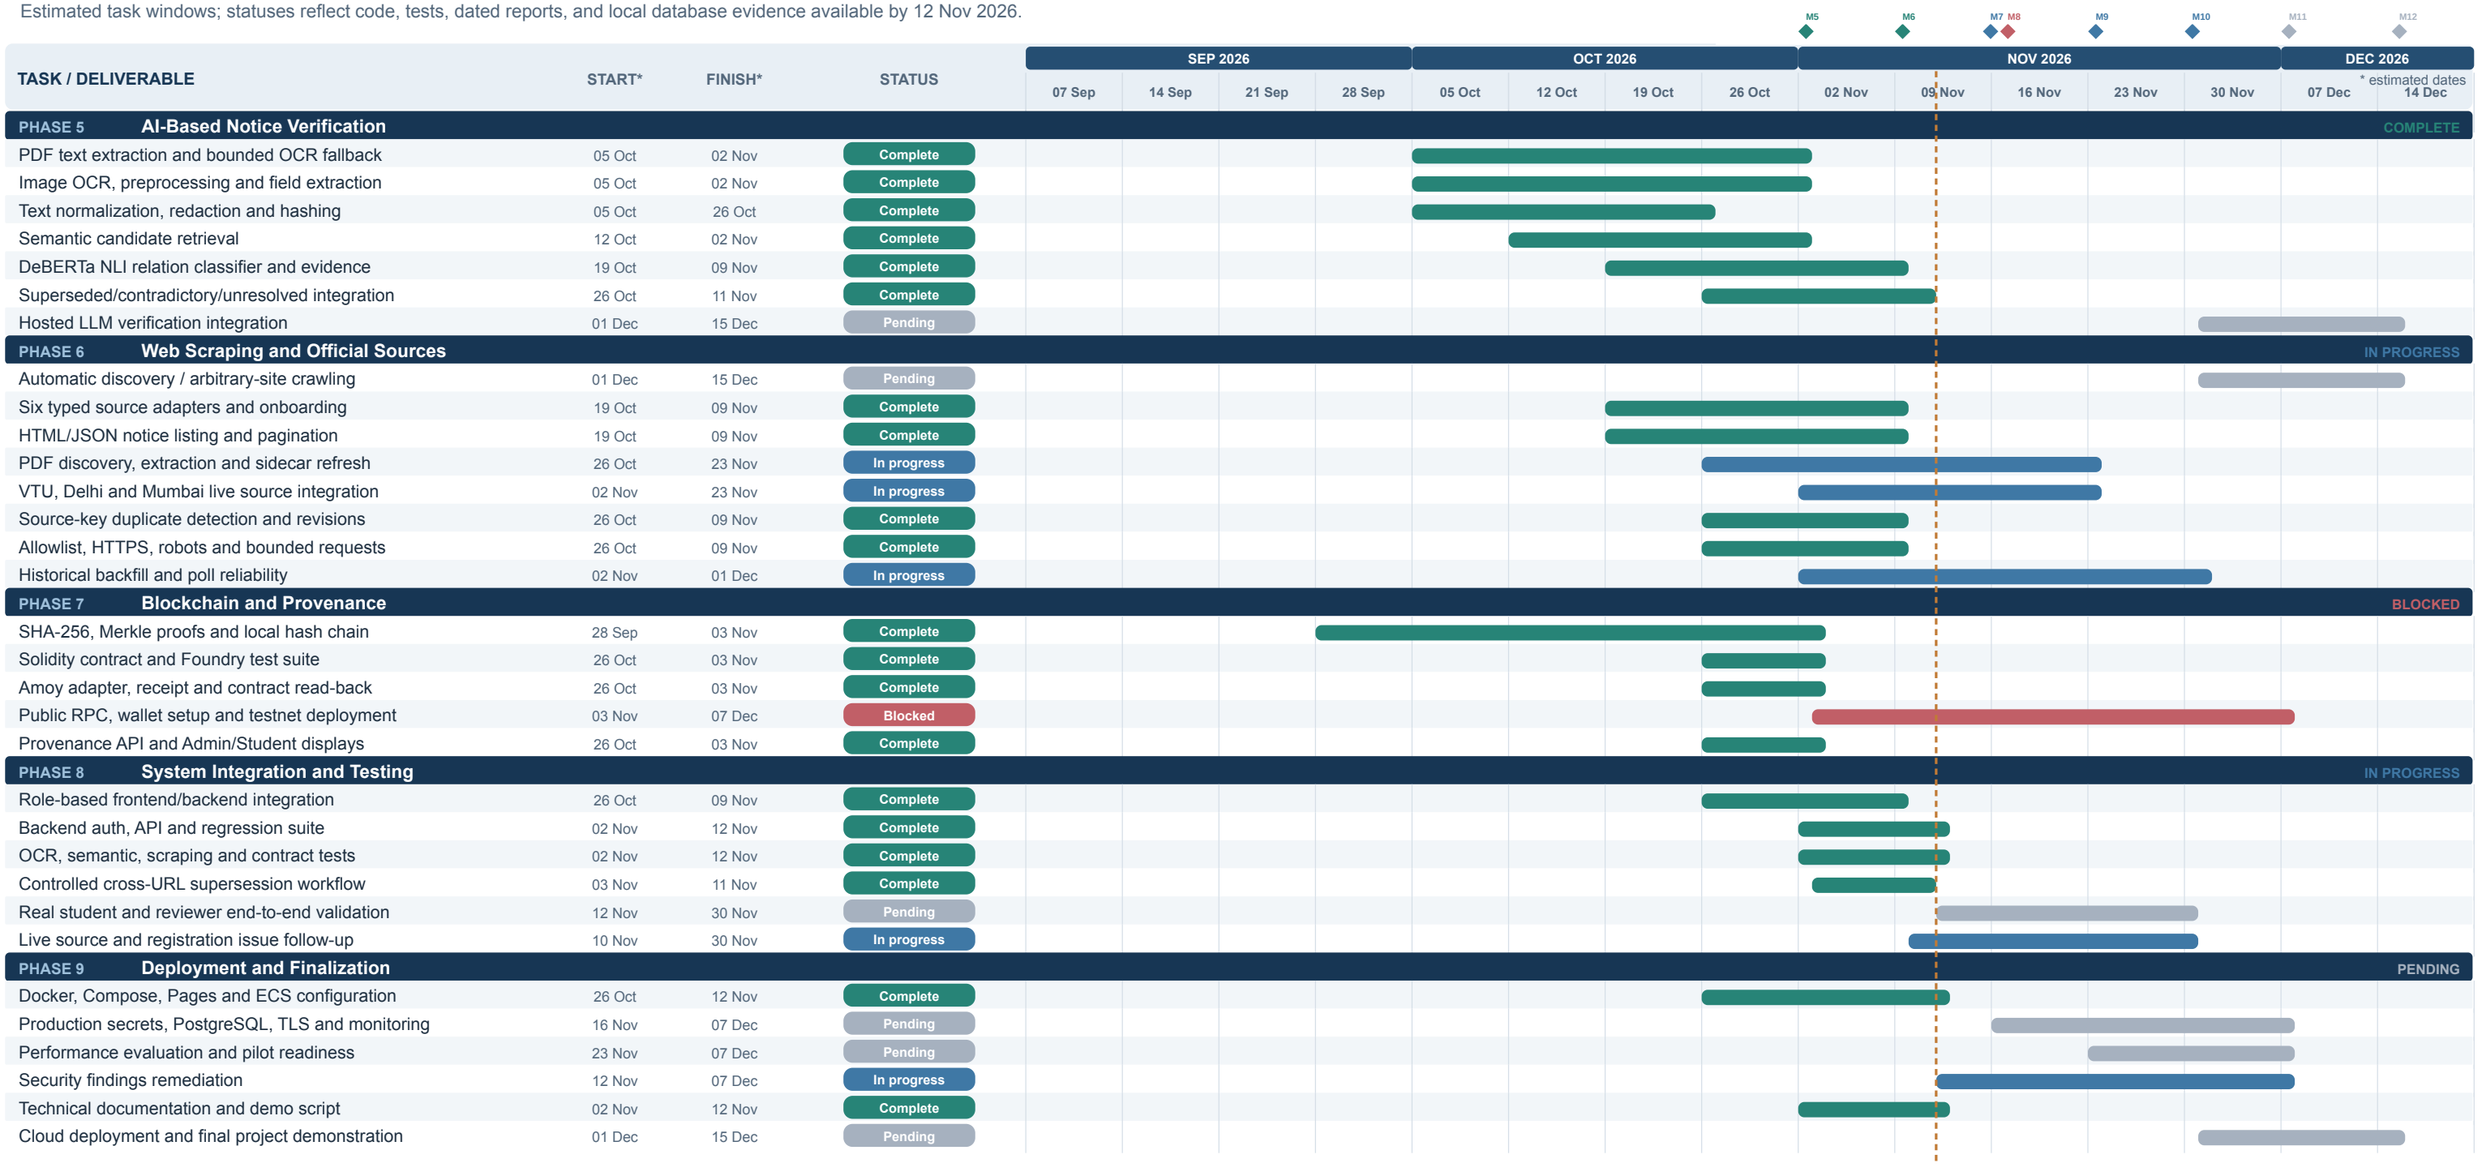

MILESTONE REGISTER

Targets are estimates; actual completion dates are not recorded unless stated in evidence notes.

- **M1 Requirements and Research Completed** — Complete
  Target 21 Sep (est.) - Requirements/design/research artifacts exist; exact completion date not recorded.
- **M2 System Architecture Finalized** — Complete
  Target 05 Oct (est.) - Architecture and database model are present; exact finalization date not recorded.
- **M3 Frontend Development Completed** — In progress
  Target 26 Oct (est.) - Core role pages exist; full Admin analytics dashboard is not implemented.
- **M4 Backend and Authentication Completed** — Complete
  Target 02 Nov (est.) - Registration/auth APIs and role tests exist; real account journey remains unverified.
- **M5 OCR and Notice Submission Implemented** — Complete
  Target 02 Nov (est.) - Upload/extraction code and tests exist; OCR requires runtime Tesseract support.
- **M6 Verification Engine Integrated** — Complete
  Target 09 Nov (est.) - Semantic/NLI integration tested on isolated controlled revision data.
- **M7 Web Scraping Integration Completed** — In progress
  Target 16 Nov (est.) - Three selected feeds active; backfills and latest source poll recovery remain.
- **M8 Blockchain Provenance Integrated** — Blocked
  Target 16 Nov (est.) - Local/Merkle and contract tests complete; public Amoy deployment not configured.
- **M9 Complete System Integration** — In progress
  Target 23 Nov (est.) - Local suite/build pass; no current product users/submissions are stored.
- **M10 Testing and Bug Fixing Completed** — In progress
  Target 30 Nov (est.) - 202 backend tests, web build and 4 contract tests pass; live-source issues remain.
- **M11 Deployment Completed** — Pending
  Target 07 Dec (est.) - Deployment templates exist; no production host/deployment is established.
- **M12 Final Project Demonstration** — Pending
  Target 15 Dec (est.) - Demo instructions exist; no completed final demonstration is recorded.

Actual dated checkpoints: 07 Sep (earliest recorded artifact, not confirmed project start); 03 Nov (Phase 2/3 reports); 10-11 Nov (source/integration reports); 12 Nov (this audit and automated checks).
